



T A N A A Z

TANAAZ – Monthly Construction Update | May 2025

Dear TANAAZ Family Members,

It gives us great pleasure to update you once again on the progress of TANAAZ.

Delivering top-quality construction and achieving possession ahead of schedule remains our constant commitment to you.

Commitment to Transparency and Quality:

This is our fifth monthly update, part of our promise to keep you regularly informed with detailed construction progress and site photographs.

We are proud to be pioneers in Ahmedabad, setting new standards in transparency and customer service through consistent and honest communication with our valued clients.

Construction Progress – May 2025

Major Construction Highlights:

- The entire basement area of Blocks A, B, and C is now fully covered with RCC slabs, creating a strong base for the building.
- Block C's Ground Floor slab has been successfully cast, providing a solid platform for the upper floors.
- All ground floor columns in Block A and Block B have been completed with strong steel reinforcement and concrete work.
- Basement mould work (temporary supports) and tying of steel rods for reinforcement are actively progressing across Blocks A, B, and C.

- Temporary mould work for the ground floor slab in Block A has started, preparing for the next level of construction.
- First-floor mould work and slab casting in Block C Part 2 are underway, marking a strong vertical movement in construction.

What's Coming Next?

- Ground floor slab temporary mould work across all blocks is close to completion.

Next Steps:

- Begin tying steel rods for beams and slabs on the first floor, followed by concrete casting.

Quality Control and Material Excellence

At TANAAZ, we maintain strict quality control at every step:

◆ Material Testing:

- Sand, cement, and aggregates are tested through field and lab tests, with all reports carefully maintained.
- Concrete cube tests are performed in-house at 7, 14, and 28 days to ensure maximum strength.

◆ Electrical Work:

- Only Polycab brand electrical conduits are used within the slabs for durability and safety.

Safety First, Always

We prioritize safety at every level:

- All workers are equipped with helmets, gloves, safety jackets, boots, PPE kits, and safety belts while working at heights.
- Construction is progressing on schedule without compromising on safety protocols.

Ahead of Schedule!

We are proud to share that we are currently 14 days ahead of our committed possession timeline — a result of careful planning, quality workmanship, and your continued trust.

Your Trust, Our Commitment

Every step we complete brings us closer to delivering a thoughtfully built, high-quality home for you and your family.

Thank you for being a part of the TANAAZ family — we look forward to sharing even more exciting updates next month!

**Warm regards,
TEAM TANAAZ**

TANAAZ – માસિક બાંધકામ અપડેટ | મે 2025

પ્રિય TANAAZ પરિવારના સભ્ય,

તમને ફરીથી TANAAZ પ્રોજેક્ટની પ્રગતિ વિશે અપડેટ આપતાં અમને ખૂબ આનંદ થાય છે.
ઉચ્ચ ગુણવત્તાવાળું બાંધકામ અને સમય પહેલાં કબજો આપવો — આ અમારા સતત વચનનો ભાગ છે.

પારદર્શિતા અને ગુણવત્તા માટે પ્રતિબદ્ધતા

આ TANAAZ તરફથી આપને મળતું પાંચમું માસિક અપડેટ છે.

અમારું વચન છે કે અમે તમને બાંધકામની પ્રગતિ અને સાર્થક ફોટા સાથે નિયમિત માહિતી આપતા રહીશું.

અમદવાદમાં અમે પારદર્શિતા અને શ્રેષ્ઠ ગ્રાહક સેવા માટે નવા ધોરણો ગોઠવી રહ્યા છીએ, અને અમારા મૂલ્યવાન ખરીદદારો સાથે વિશ્વસનીય અને ખુલ્લી વાતચીત દ્વારા આ પદ્ધતિ આગળ વધારી રહ્યા છીએ.

બાંધકામની પ્રગતિ – મે 2025

મુખ્ય બાંધકામ તબક્કા :

- બ્લોક A, B અને C ના આખા બેઝમેન્ટ વિસ્તારમાં RCC સ્લેબનું કામ પૂર્ણ થયું છે, જે મજબૂત આધાર પૂરો પાડી રહ્યું છે.
- બ્લોક C ના ગ્રાઉન્ડ ફ્લોર સ્લેબનું કામ સફળતાપૂર્વક પૂરું થયું છે, જે ઉપરના માળાઓ માટે મજબૂત પાટો પૂરું પાડે છે.
- બ્લોક A અને B ના તમામ ગ્રાઉન્ડ ફ્લોર કોલમ્સ સ્ટીલ અને કોંક્રિટ વડે પૂરું કરવામાં આવ્યા છે.
- બેઝમેન્ટ માટેનું ટેમ્પરરી મોલ્ડ વર્ક અને સ્ટીલ રોડ બાંધવાનું કામ (ટાઈંગ) બ્લોક A, B અને C માં સતત ચાલી રહ્યું છે.

- બ્લોક A માટે ગ્રાઉન્ડ ફ્લોર સ્લેબ માટે મોલ્ડ વર્ક (ટેમ્પરરી સપોર્ટ) શરૂ થયું છે, જેથી આગળના માળ માટે તૈયારી થઈ શકે.
- બ્લોક C (પાર્ટ 2) માં ફર્સ્ટ ફ્લોર માટે મોલ્ડ વર્ક અને કોંક્રિટ કાસ્ટિંગનું કામ ચાલુ છે, જે બિલ્ડિંગના ઉપરના માળ માટેનો મહત્વપૂર્ણ તબક્કો દર્શાવે છે.

આગળ શું આવશે?

- તમામ બ્લોકસમાં ગ્રાઉન્ડ ફ્લોર માટે મોલ્ડ વર્ક લગભગ પૂર્ણ થવામાં આવ્યું છે.
- પ્રથમ માળ માટે બીમ અને સ્લેબ માટે સ્ટીલ રોડ બાંધવાનું કાર્ય શરૂ થશે, અને પછી કોંક્રિટ કાસ્ટિંગ કરવામાં આવશે.

ગુણવત્તા નિયંત્રણ અને શ્રેષ્ઠ સામગ્રી

TANAAZ ખાતે, દરેક તબક્કે કડક ગુણવત્તા નિયંત્રણ જાળવવામાં આવે છે:

સ. ા. મગ્રી નું પરીક્ષણ:

- રેતી, સિમેન્ટ અને એગ્રીગેટ્સનું ફીલ્ડ અને લેબ ટેસ્ટિંગ થાય છે અને તમામ રિપોર્ટ્સ જાળવવામાં આવે છે.
- કોંક્રિટના ક્યુબ ટેસ્ટ (7, 14 અને 28 દિવસના) સાઈટ પર અમારી પોતાની ટેસ્ટિંગ મશીનો પર કરવામાં આવે છે.

◆ વિદ્યુત કાર્ય:

- દરેક સ્લેબમાં માત્ર પોલીકોબ બ્રાન્ડના વિદ્યુત કન્ડ્યુટ પાઈપ્સનો ઉપયોગ થાય છે, લાંબા ગાળાની સલામતી અને ટકાઉપણું સુનિશ્ચિત કરવા માટે.

સૌપ્રથમ સલામતી

સાઈટ પર દરેક કર્મચારી માટે સલામતી મહત્વપૂર્ણ છે:

- દરેક કામદારો હેલ્મેટ, ગ્લોવ્સ, સેફ્ટી જેકેટ્સ, બૂટ્સ, PPE કિટ્સ અને ઊંચાઈ પર સેફ્ટી બેલ્ટ્સ સાથે કામ કરે છે.
- બાંધકામનું કાર્ય સમયપત્રક મુજબ સચોટ રીતે આગળ વધી રહ્યું છે, સલામતીના તમામ નિયમોનું પાલન કરતી વખતે.

અમે સમય કરતાં આગળ છીએ!

ગર્વથી જણાવી શકીએ છીએ કે TANAAZનો બાંધકામ હાલમાં અમારા નિર્ધારિત કબજાના સમય કરતાં 14 દિવસ આગળ છે — જેનો શ્રેય સારી યોજના, શ્રેષ્ઠ બાંધકામ અને આપના વિશ્વાસને છે.

તમારો વિશ્વાસ, અમારું વચન

દરેક તબક્કા સાથે, **TANAAZ** તમારા માટે વિચારપૂર્વક રચાયેલ અને ઉચ્ચ ગુણવત્તાવાળું ઘર પૂરું પાડવાની તરફ આગળ વધી રહ્યું છે.

TANAAZ પરિવારનો ભાગ બનવા બદલ તમારો દિલથી આભાર!

આગામી મહિને વધુ રોમાંચક પ્રગતિ સાથે મળવાની આતુરતા છે.

હાર્દિક શુભેચ્છાઓ સાથે,
TANAAZ ટીમ




RCC Slab Completed for Basement (Blocks A, B, and C)

The entire basement area of Blocks A, B, and C is now fully covered with RCC slab, creating a strong foundation for the buildings.



Block C Ground Floor Slab Completed

Ground floor slab casting for Block C has been successfully completed, providing a solid and stable base for upper floors.

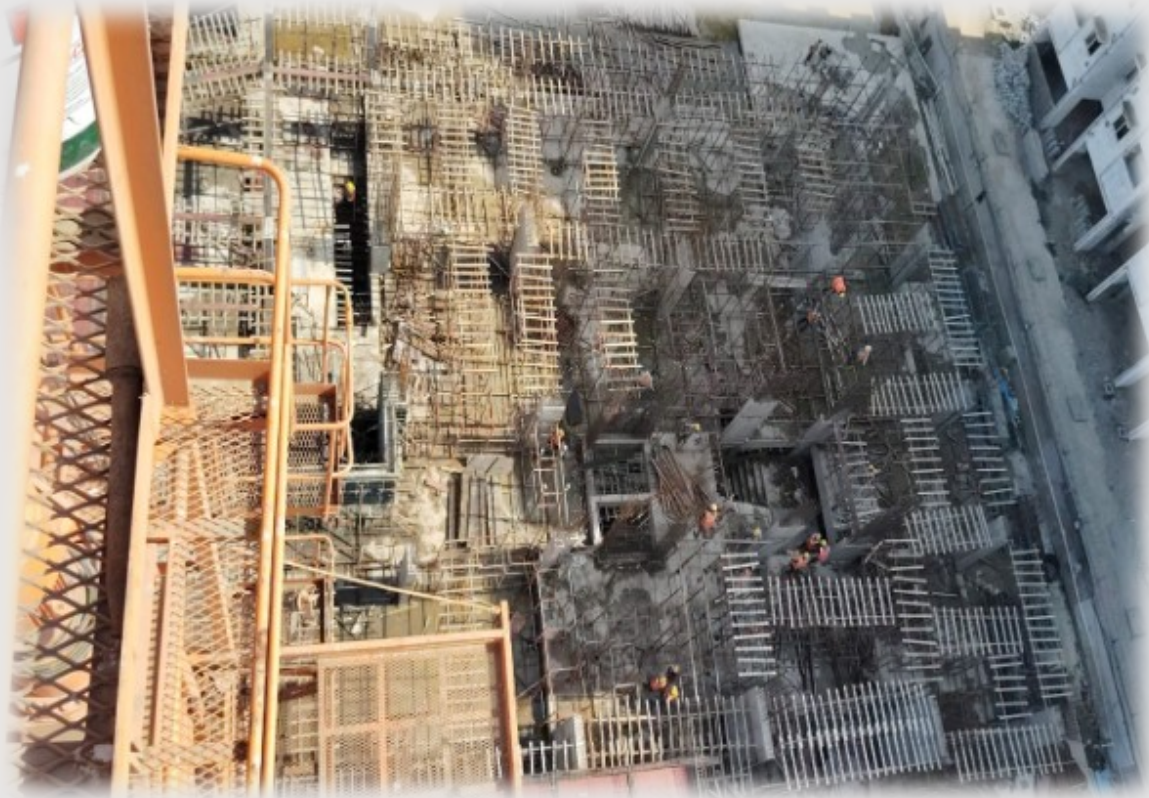

Ground Floor Columns Completed – Block A and Block B

All ground floor columns in Block A and Block B are complete with strong steel and concrete work, forming the building's core support.



Mould Work and Steel Rod Tying in Basement (Blocks A, B, and C)

Temporary moulds and tying of steel rods for reinforcement are actively progressing across all basement areas.



Ground Floor Mould Work Started – Block A

Temporary mould work (shuttering) for the ground floor slab has started in Block A, moving closer to slab casting.



First Floor Mould Work and Slab Casting in Progress and – Block C (Part 2)

Work for the first-floor slab, including mould setup and concrete casting, is underway in Block C Part 2.
