



T A N A A Z

## TANAAZ – Monthly Construction Update | July 2025

Dear TANAAZ Family Members,

We're pleased to bring you our seventh monthly update on the progress at TANAAZ.

Each step brings us closer to delivering your thoughtfully designed, high-quality home — and we remain ahead of schedule, thanks to disciplined execution and careful planning.

### Note on Weather Conditions

Unexpected rainfall in May created minor delays in a few activities. As we now enter the core monsoon season, our team is closely monitoring weather conditions and adjusting timelines as needed. While rain does present challenges, our engineering and safety teams are fully prepared to manage these with minimal disruption.

### Commitment to Transparency and Quality

TANAAZ is proud to lead by example in Ahmedabad's real estate market by providing regular, honest, and detailed construction updates.

Thank you for your trust — it keeps us motivated to build better every day.

### Construction Progress – July 2025

#### This Month's Highlights:

#### Block C

- 2nd floor RCC slab casting completed
- 3rd floor column work completed
- 3rd floor slab casting in progress

### **Block B**

- 2nd floor RCC slab casting completed
- 3rd floor slab shuttering in progress

### **Block A & B**

- Ground floor masonry work started

### **Block C**

- 1st floor masonry in progress

### **What's Next**

- Block B: 3rd floor slab casting
- Block C: Completion of 3rd floor slab

**Electrical:** Installation of conduits and switch boxes in Block C (1st floor) and ground floor areas

### **Design & Quality Control**

#### **◆ AAC Block Plant Visit**

- To ensure the quality and durability of materials used, our engineering team visited the AAC block production facility. Every batch used on site is checked to meet structural and performance standards.

#### **◆ Parking Planning Partner Onboarded**

- We are pleased to welcome as the official parking design and management consultants for TANAAZ.

**Their role includes:**

- Designing efficient, user-friendly parking layouts across all blocks
- Ensuring compliance with RERA, safety, and local regulations
- Planning visitor parking, EV charging, accessible bays, and two-wheeler zones
- Supporting architectural teams with input on ventilation, slope, markings, and signage
- Helping us create a future-ready parking experience that is safe, practical, and easy to navigate for all residents and visitors

### **Environmental Health & Safety (EHS)**

- A real-time dust monitoring system has been installed on site to track air quality and reduce environmental impact
- Regular mosquito fogging, cleaning, and housekeeping are carried out to maintain hygiene
- All workers use PPE kits including helmets, gloves, belts, and boots — ensuring full safety compliance

### **Ahead of Schedule!**

We are proud to report that TANAAZ remains 12 days ahead of our committed possession timeline — a testament to planning, precision, and teamwork.

### **Your Trust, Our Commitment**

**Every floor, every slab, and every brick is being placed with care.**

Thank you for being part of the TANAAZ family — we look forward to bringing you more exciting updates next month.

**Warm regards,  
TEAM TANAAZ**

પ્રિય **TANAAZ** પરિવારના સભ્ય,

અમે TANAAZ પ્રોજેક્ટની પ્રગતિ અંગે આપને સાતમું માસિક અપડેટ આપવા આનંદ અનુભવી રહ્યા છીએ.

મે મહિનાના આગુધાર્યા વરસાદના કારણે અમુક કામગીરીમાં વિલેપ આવ્યો હતો. હવે જ્યારે ચોમાસા ની ઋતુ શરૂ થઈ ગઈ છે, ત્યારે અમારી ટીમ પરિસ્થિતિનું ધ્યાનપૂર્વક નિરીક્ષણ કરી રહી છે અને તે મુજબ કામગીરીને ગોઠવી રહી છે. ધીમી ગતિની પરિસ્થિતિમાં પણ અમે ગુણવત્તા અને સમયપત્રક જાળવી રાખવાનો સંપૂર્ણ પ્રયાસ કરી રહ્યા છીએ.

પારદર્શિતા અને ગુણવત્તા માટે પ્રતિબદ્ધતા :

TANAAZ એ અમદાવાદમાં ગુણવત્તા અને પારદર્શિતા માટે ઊંચો ધોરણ નિર્ધારિત કર્યો છે. દર મહિને આપને નક્કર અપડેટ આપીને, અમે આપને દરેક તબક્કે જોડાયેલા રાખવા માટે પ્રતિબદ્ધ છીએ.

બાંધકામની પ્રગતિ – જુલાઈ 2025

મુખ્ય તબક્કાઓ

**બ્લોક C:**

- બીજું માળ RCC સ્લેબ પૂરું.
- ત્રીજા માળના કોલમ કાર્ય પૂર્ણ.
- સ્લેબ કાર્સિટિંગ ચાલુ.

**બ્લોક B:**

- બીજું માળ RCC સ્લેબ પૂર્ણ.
- ત્રીજું માળ તૈયાર થઈ રહ્યું છે.

બ્લોક A અને B:

- ગ્રાઉન્ડ ફ્લોર ચણતર શરૂ.

બ્લોક C:

- પહેલો માળ ચણતર ચાલુ છે.

આગળ શું છે

- બ્લોક B: ત્રીજા માળનું સ્લેબ કાસ્ટિંગ.
- બ્લોક C: ત્રીજા માળનું સ્લેબ કાસ્ટિંગ પૂર્ણ.

ઇલેક્ટ્રિકલ કાર્ય: ગ્રાઉન્ડ ફ્લોર અને બ્લોક C ના પહેલો માળ - કન્ડ્યુટ અને બોક્સ સ્થાપનાડિઝાઈન અને ગુણવત્તા નિયંત્રણ

◆ AAC બ્લોક પ્લાન્ટ મુલાકાત:

- અમારી એન્જિનિયરિંગ ટીમે પ્લાન્ટની મુલાકાત લઈને ગુણવત્તા સુનિશ્ચિત કરી.

પાકિંગ અમો જન સહયોગી :

- TANAAZ માટે અધિકૃત પાર્કિંગ ડિઝાઈન અને મેનેજમેન્ટ કન્સલ્ટન્ટ તરીકે જોડાયા છે.

તેમની જવાબદારીઓમાં શામેલ છે:

- સહેલાઈથી વાપરી શકાય તેવી પાર્કિંગ ડિઝાઇન તૈયાર કરવી
- RERA અને લોકલ બિલ્ડિંગ નિયમો અનુસાર પ્લાનિંગ
- વિઝિટર, EV ચાર્જિંગ અને વ્યાપારી પાર્કિંગ માટે સુવિધા
- સંપૂર્ણ ડિઝાઇન માટે ટેકનિકલ માર્ગદર્શન

પર્યાવરણીય સ્વાસ્થ્ય અને સલામતી

- ધૂળ નિયંત્રણ માટે સાઈટ પર રિયલ-ટાઈમ dust મોનિટર ઈન્સ્ટોલ કરાવું છે
- નિયમિત fogging, સાક્ષકાઈ અને housekeeping જાળવવામાં આવે છે
- તમામ શ્રમિક PPE કિટ (હેલ્મેટ, ગ્લોવ્સ, બૂટ, બેલ્ટ) સાથે કાર્ય કરે છે

અમે સમય કરતાં આગળ છીએ!

**TANAAZ** હાલમાં નિર્ધારિત સમયપત્રક કરતાં **12** દિવસ આગળ ચાલી રહ્યું છે — અમારી ટીમના આયોજન અને કાર્યક્ષમતા માટે આ આભાર છે.

તમારું વિશ્વાસ, અમારું વચન

દરેક તબક્કો **TANAAZ** માં આપના નવા ઘરની નજીક લઈ જાય છે. **TANAAZ** પરિવારનો ભાગ બનવા બદલ આભાર.

હાર્દિક શુભેચ્છાઓ સાથે,

**TANAAZ** ટીમ




## Block C

- 2nd Floor Slab Completed, 3rd Floor Work in Progress
- Concrete casting for the 2nd floor is complete. Column work is done, and slab work is now in progress on the 3rd floor.



## Ground Floor Masonry – Block A & B

- Brickwork has begun on the ground floor of both Blocks A and B, marking the start of interior wall development.

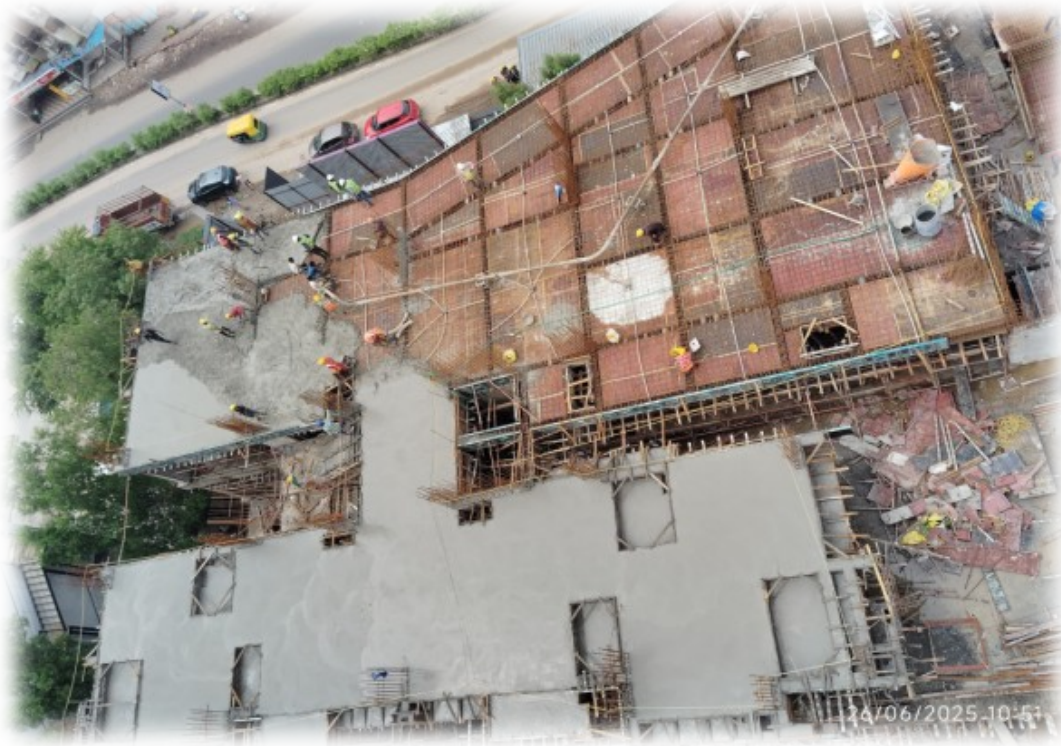

### Top View – Block B

- Bird's-eye view of Block B showing completed 2nd floor slab and ongoing work on upper levels.



### Top View – Block C

- Progress view showing finished 2nd floor slab and 3rd floor slab shuttering underway.



## AAC Block Plant Visit

- TANAAZ engineers inspecting the production of AAC blocks — ensuring only high-quality materials are used.



## Real-Time Dust Monitoring at Site

- This sensor-based system tracks dust levels continuously, helping the team keep the environment safe for workers and neighbors.



### Front Elevation – Block A & B

- Current front view of Blocks A and B, showcasing structure and masonry progress.



### Front Elevation – Block A

- Closer elevation view of Block A — structural work visibly progressing upwards.
